


CONSTRUCTION APPROACH SIGNING

SEE STD E-100M FOR SIGN PLACEMENT

NOT TO SCALE

LEGEND

RWA = ROAD WORK AHEAD
RW500 = ROAD WORK 500'
RWN = ROAD WORK NEXT XX MILES
ERW = END ROAD WORK
RPA = RAMP PAVING AHEAD

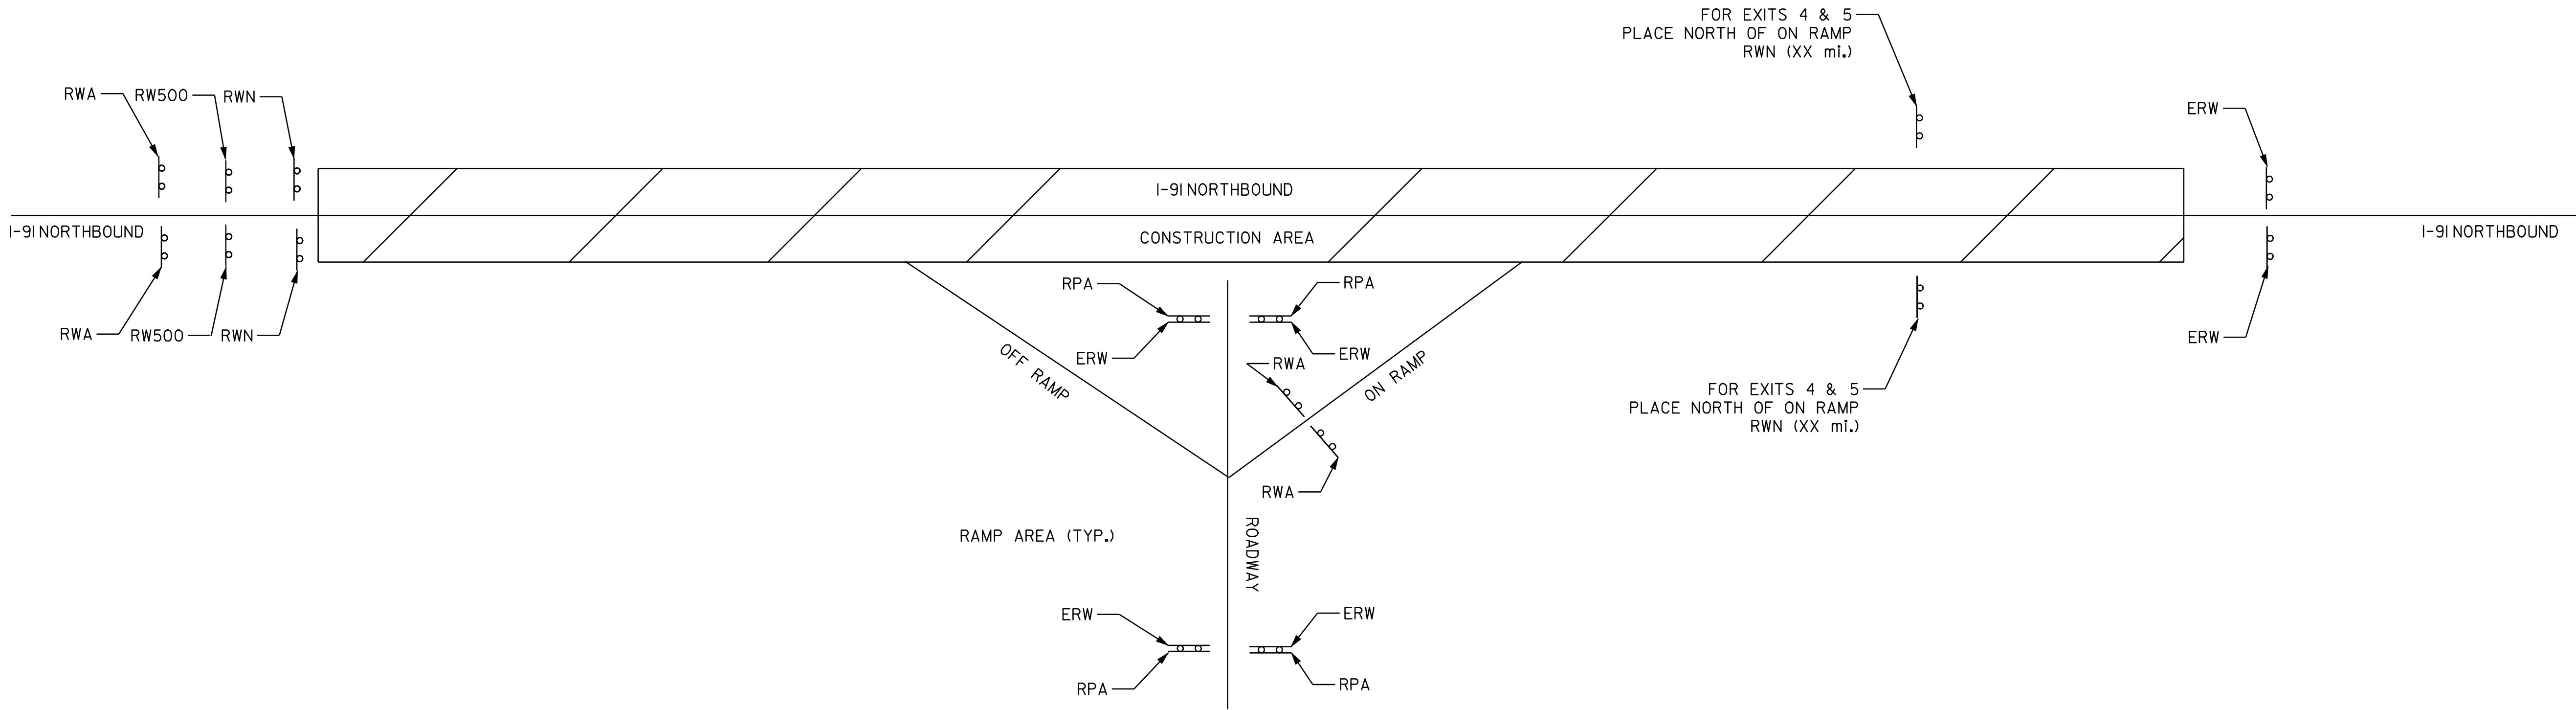

NOTES:

1. ADDITIONAL RAMP SIGNING MAY BE REQUIRED AS DIRECTED BY THE RESIDENT ENGINEER.
2. THE BID PRICE FOR TRAFFIC CONTROL - ITEM 641.10, SHALL INCLUDE ALL APPROACH AND ON-PROJECT CONSTRUCTION SIGNING, BARRIERS, BARRELS, CONES, BARRICADES, TEMPORARY REGULATORY AND WARNING SIGNS, POSTS AND PORTABLE MESSAGE SIGNS AS DETAILED IN STANDARD E-103M. ALL ADJUSTING, RELOCATING AND REMOVING OF THESE DEVICES AS DIRECTED BY THE RESIDENT ENGINEER, SHALL BE INCLUDED.THE FOLLOWING ITEMS WILL BE PAID UNDER THEIR SPECIFIC BID PRICES:

646.614, .615, AND .70 - TEMPORARY MARKINGS
630.10, .15 - UNIFORMED TRAFFIC OFFICERS AND FLAGGERS
3. FOUR (4) PORTABLE CHANGEABLE MESSAGE SIGNS WILL BE PROVIDED FOR USE ALONG THE NORTHBOUND LANES AND ON - RAMP OF INTERSTATE 91. THE PLACEMENT OF THESE MESSAGE SIGNS AS WELL AS THEIR MESSAGES WILL BE AS APPROVED BY THE RESIDENT ENGINEER. THIS QUANTITY IS PAID FOR AS PART OF ITEM 641.15 - PORTABLE CHANGEABLE MESSAGE SIGN.

TOWN/STATE HIGHWAY NAME	ROAD WORK AHEAD	END ROAD WORK	ROAD WORK 500'	ROAD WORK NEXT 18 MILES	ROAD WORK NEXT 11 1/2 MILES	RAMP PAVING AHEAD
I-91 NORTHBOUND						
BEGINNING OF PROJECT	2		2	2		
EXIT 4 INTERCHANGE	2	4				4
STATION 29+623					2	
EXIT 5 INTERCHANGE	2	4				4
END OF PROJECT		2				
TOTAL	6	10	2	2	2	8

NOTE: ALL DIMENSIONS IN METERS EXCEPT AS INDICATED

CONSTRUCTION APPROACH SIGNING	PROJECT NAME: BRATTLEBORO - WESTMINSTER	
	PROJECT NUMBER: IM 091-(141)	
	FILE NAME: /pave/01a008/pa008.dgn	PLOT DATE: 06-APR-2005 11:5
	PROJECT LEADER: WRH	DRAWN BY: JAC
	DESIGNED BY:	CHECKED BY: PTS
	IPARM NAME: pa008cas.1	SHEET 24 OF 24
