

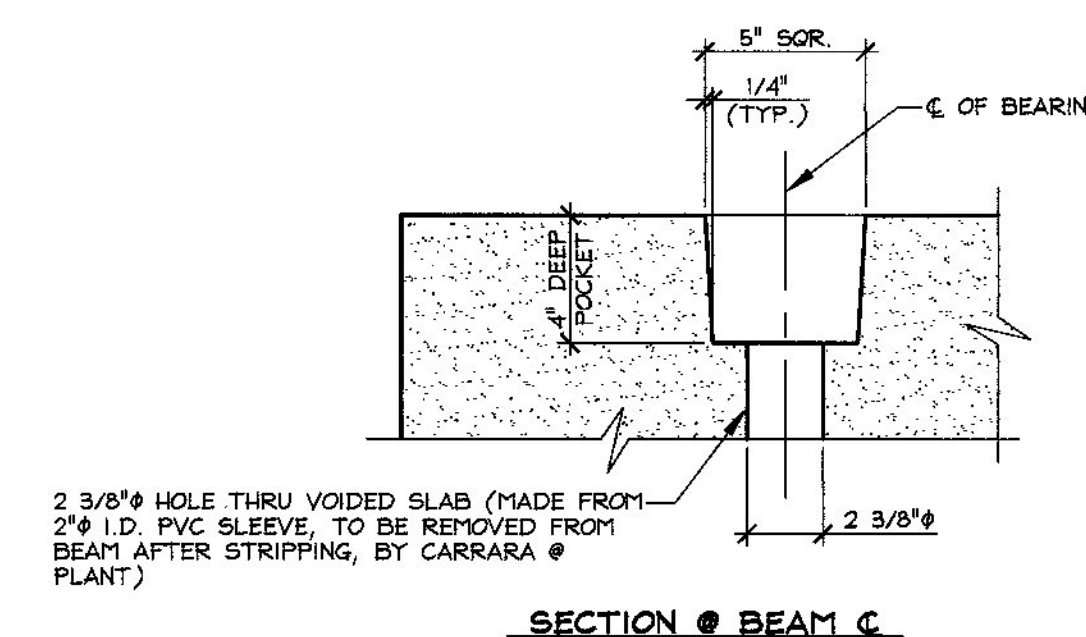
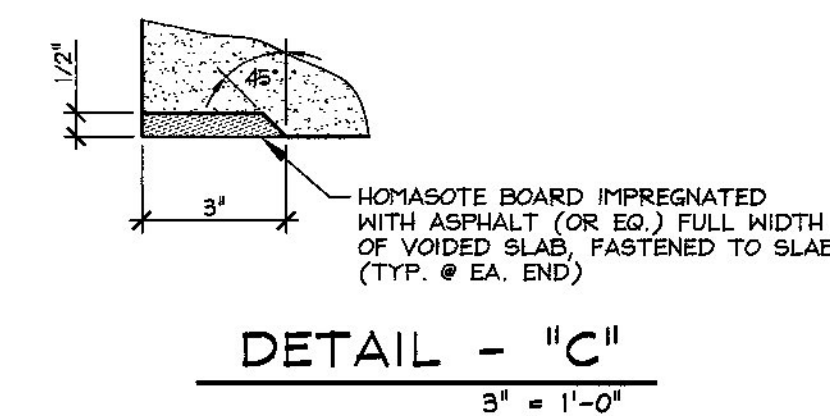
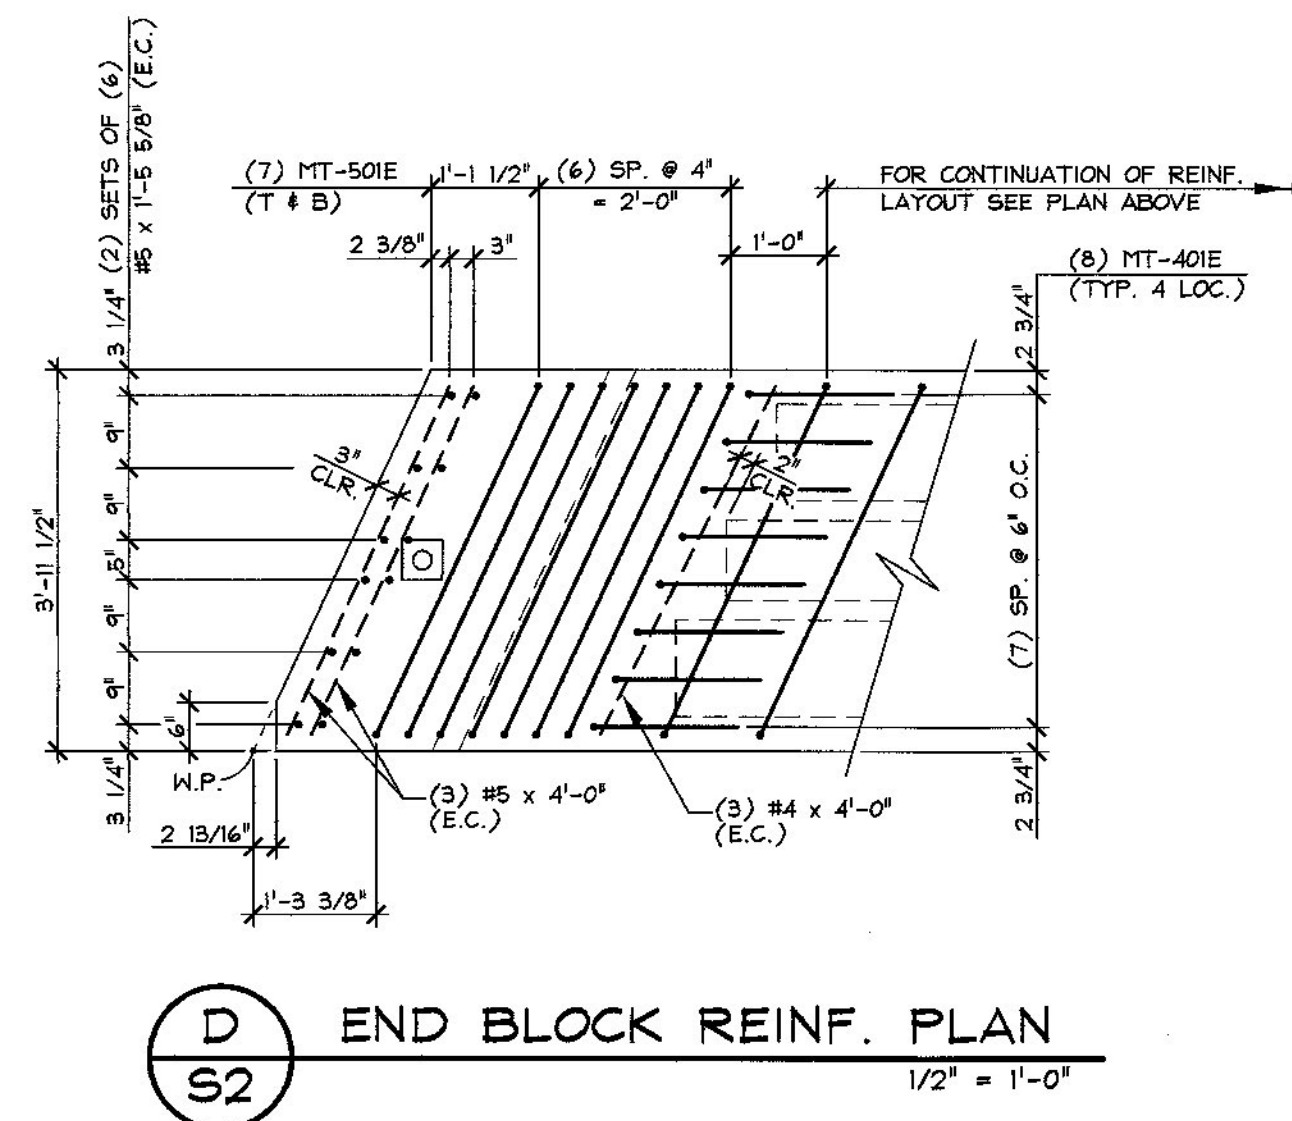
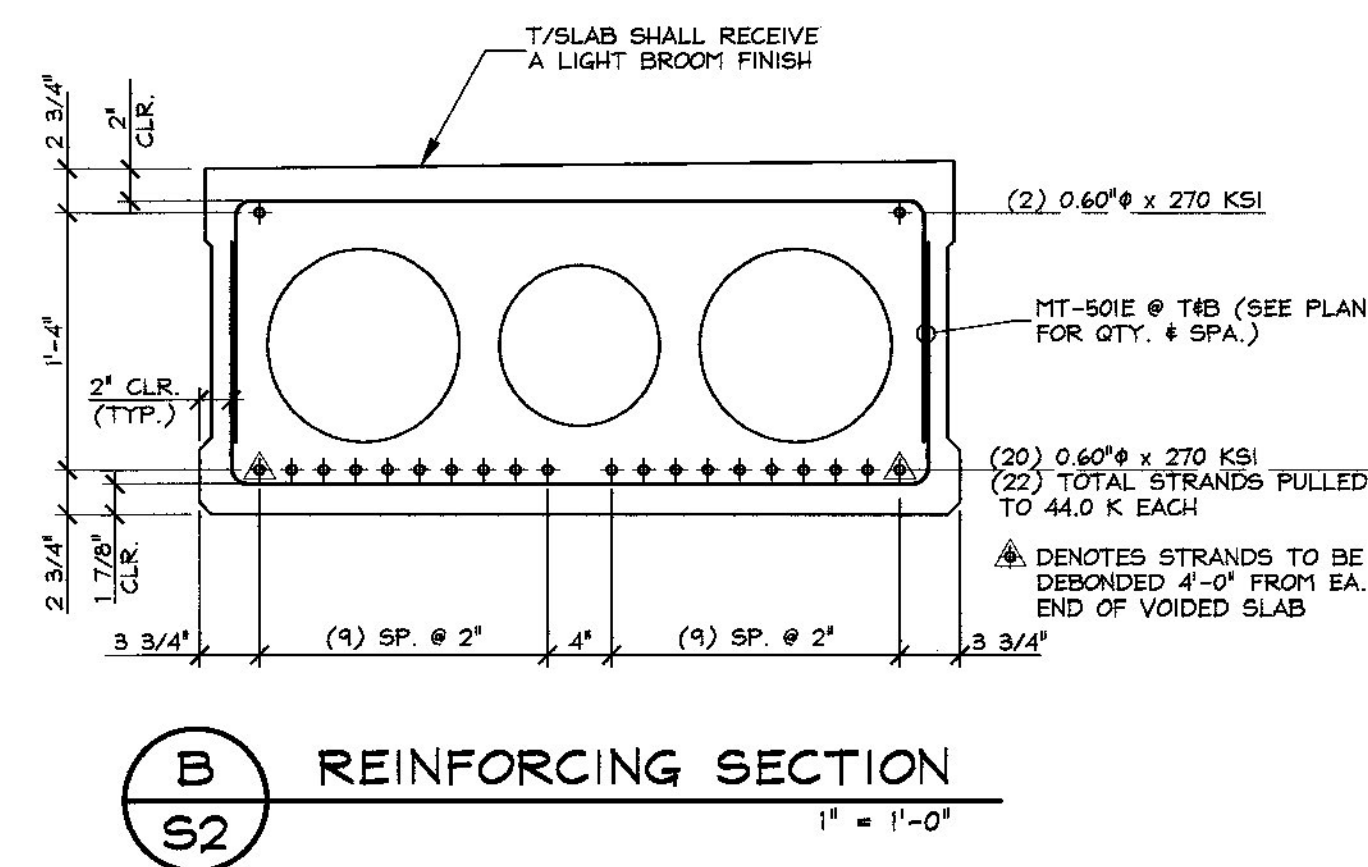
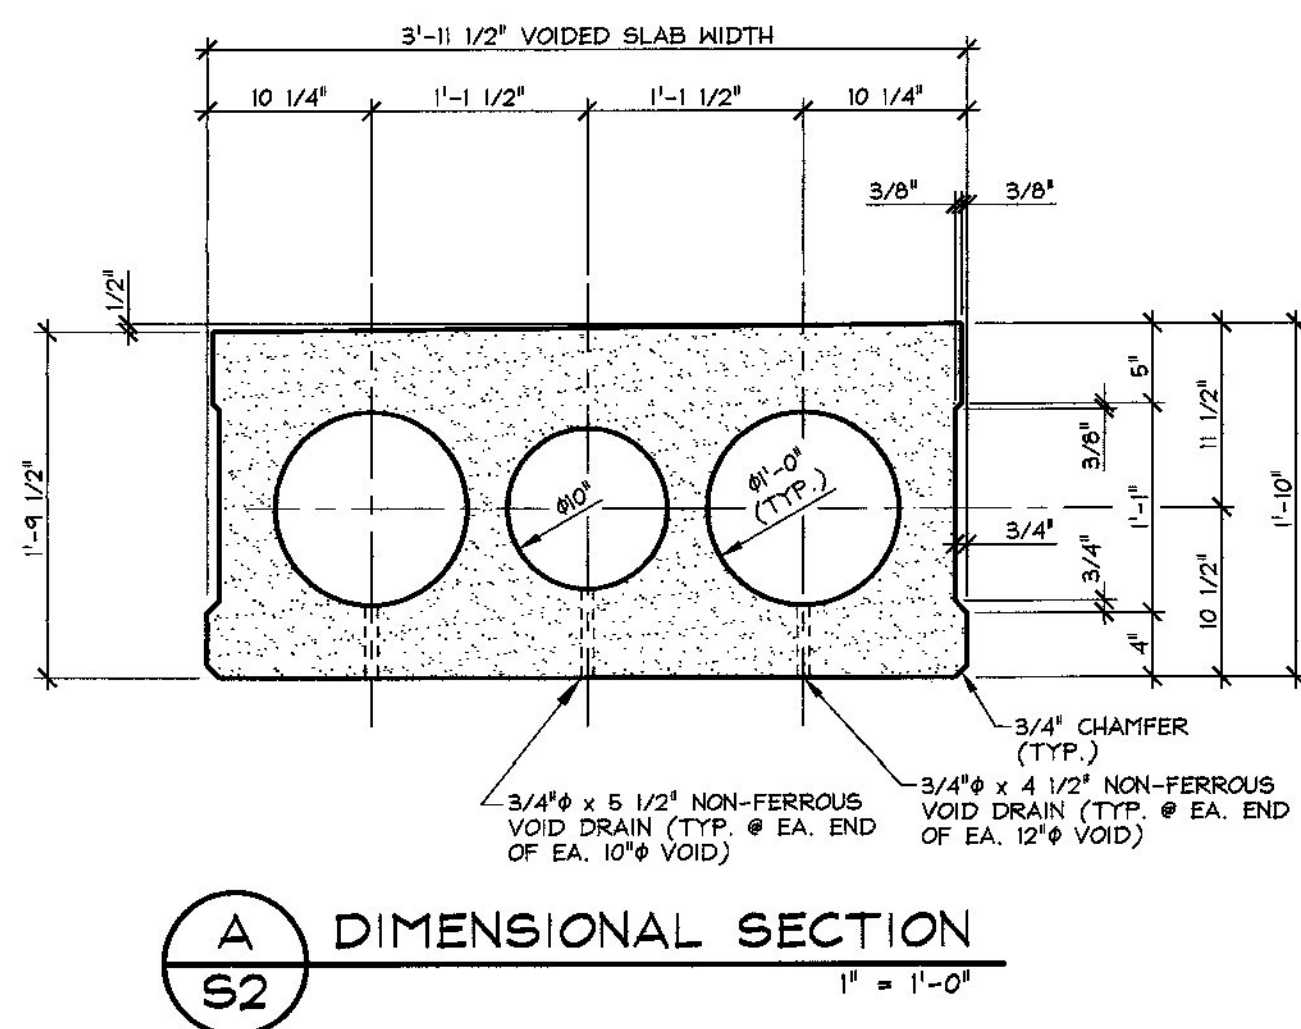
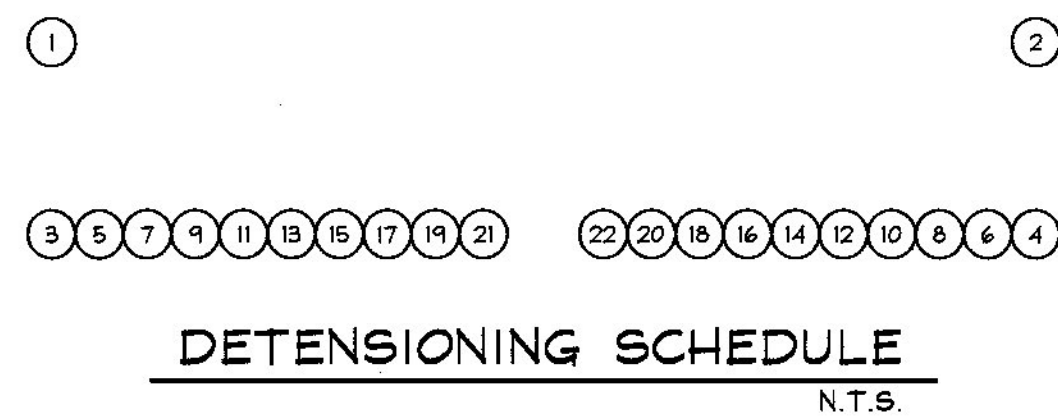
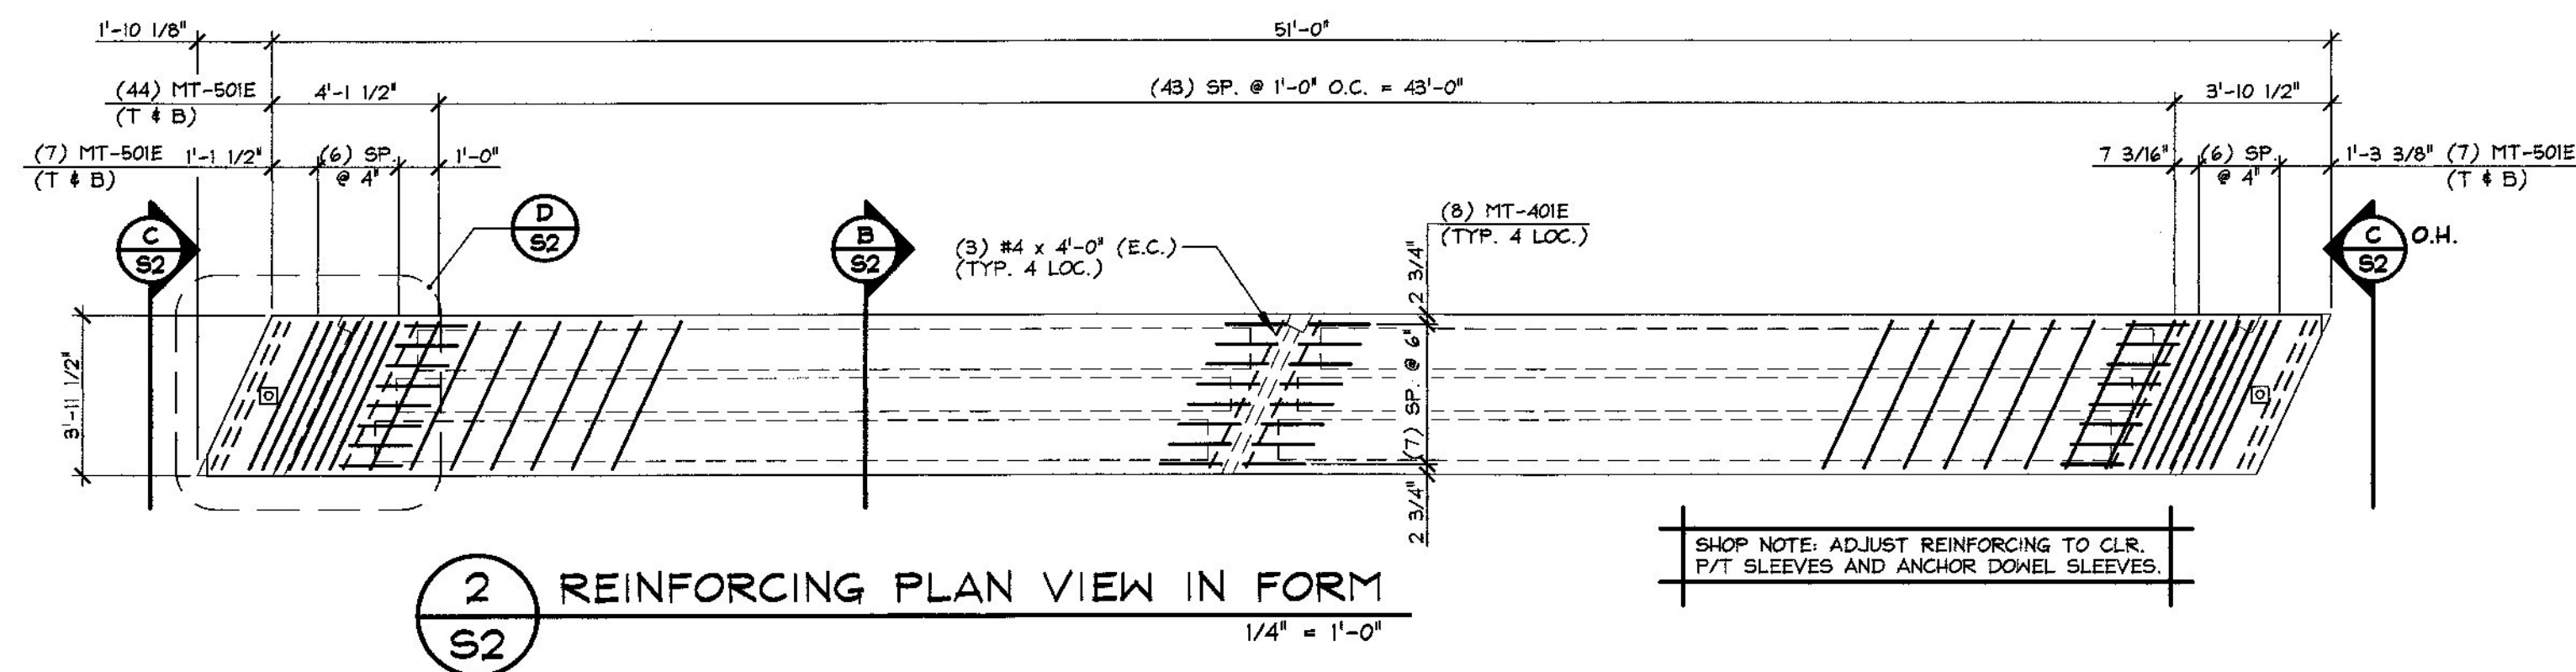


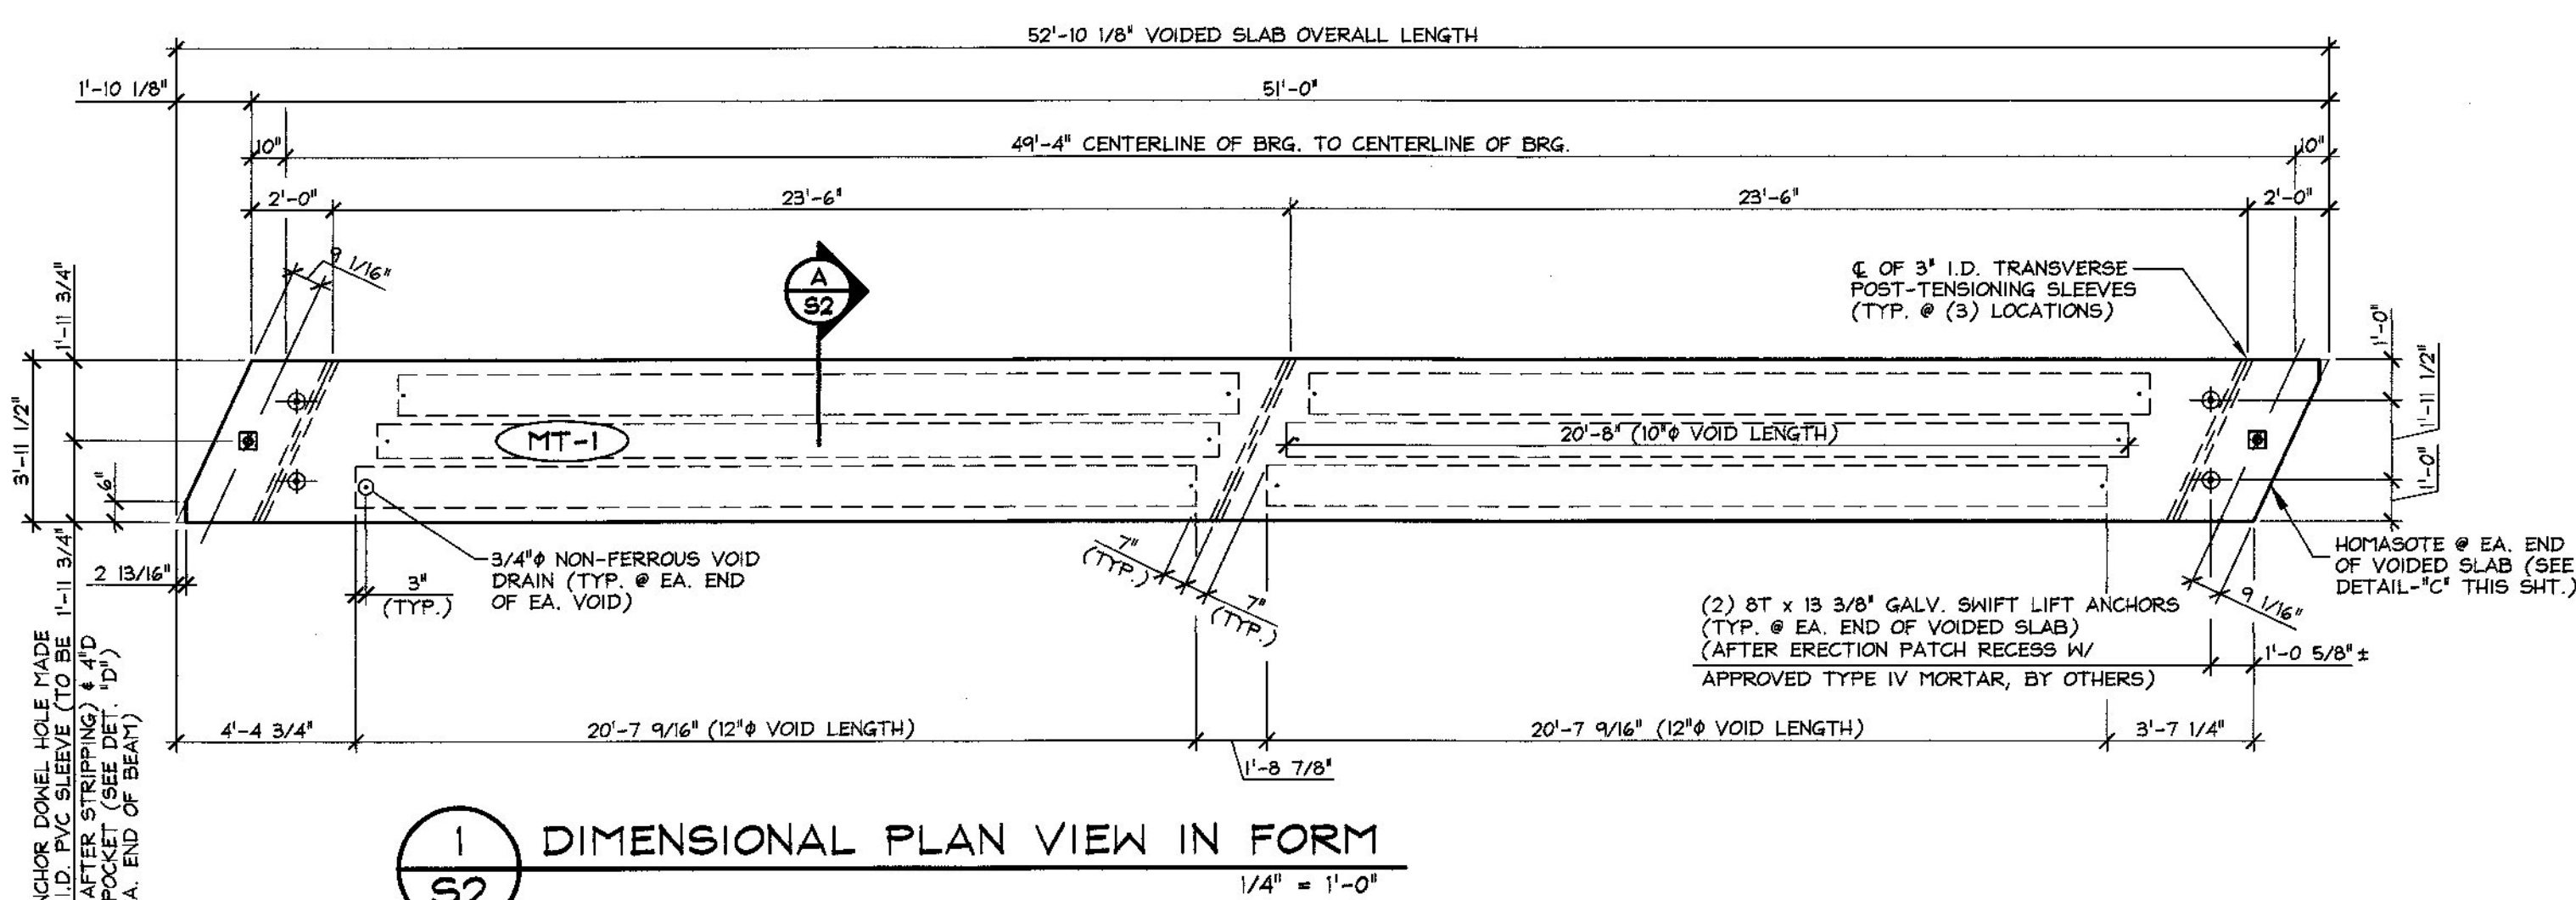

Vermont Agency of Transportation
RECEIVED
 CK'D BY HIS OK'D BY MRU
 May 23, 2014
 RESUBMIT NO Approved
 BY Carolyn Carlson DATE June 4, 2014

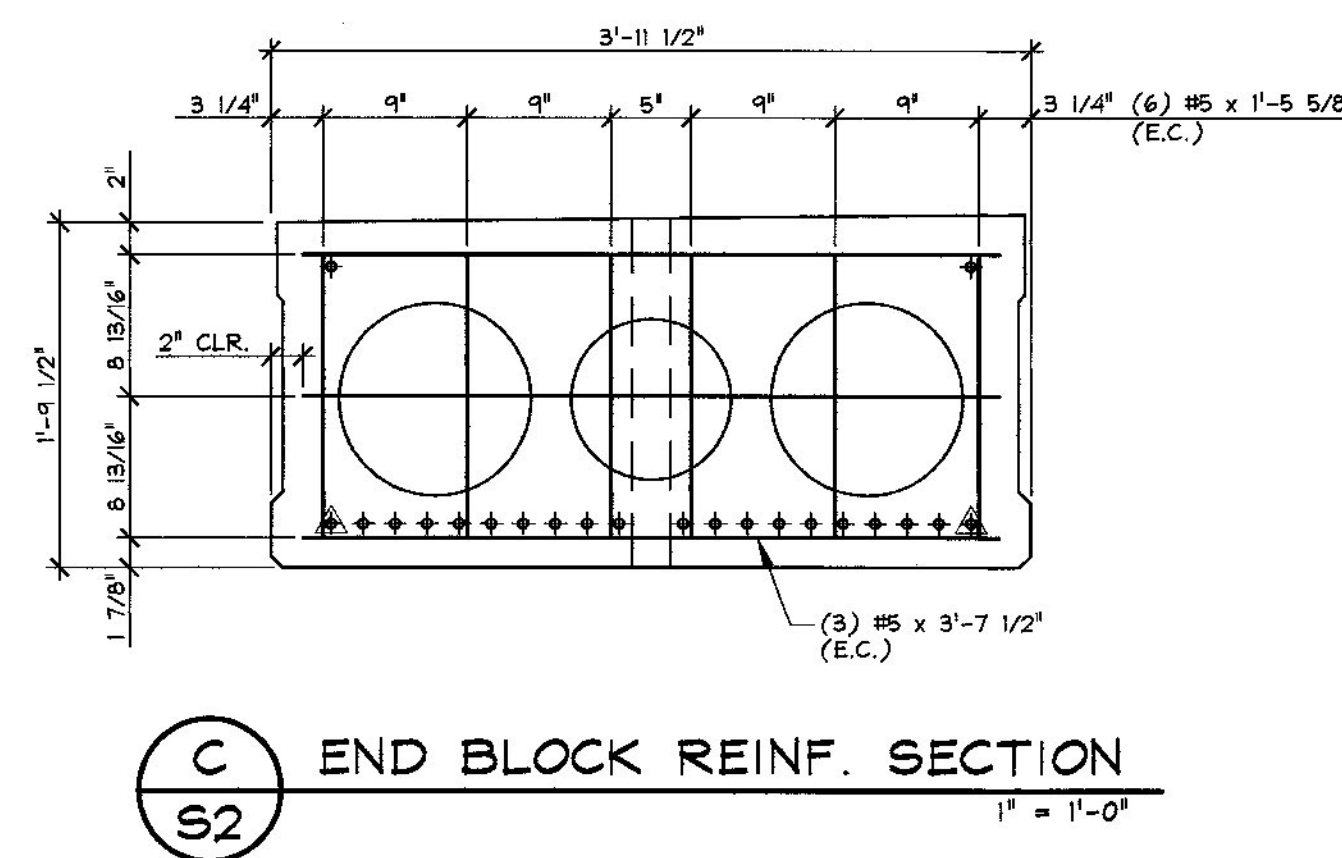

MARK: MT-1	QTY.: 2	WT.: 19.94 T	VOL.: 9.85 cy
MATERIAL LIST / SLAB			
ITEM	MARK	DESCRIPTION	QTY./SLAB
1			MT-1
2	MT-401E	#4 BENT BAR (LEVEL 1 EPOXY COATED)	32
3	MT-501E	#5 BENT BAR (LEVEL 1 EPOXY COATED)	116
4			
5			
6			
7			
8			
9		#4 x 4'-0" (LEVEL 1 EPOXY COATED)	12
10		#5 x 4'-0" (LEVEL 1 EPOXY COATED)	24
11			
12			
13			
14			
15			
16			
17		12" x 20'-7 9/16" VOID	4
18		10" x 20'-8" VOID	2
19			
20		8T x 13 3/8" SHIFT LIFT ANCHORS (GALV.)	4

APPROVAL STAMP:		J.P. CARRARA & SONS INC. AL ST. ONGE CONTRACTORS, INC. Precast & Prestress Manufacturer 2404 DISE STR., MIDDLEBURY, VERMONT 05753 Phone: (802) 388-6361 Fax: (802) 388-8010	
STATE OF VERMONT AGENCY OF TRANSPORTATION COUNTY OF FRANKLIN		DATE: MARCH 10, 2014 SCALE: NOTED	
TOWN OF MONTGOMERY ROUTE NO. TH 10 CLASS 3 BRIDGE NO.: 36 PROJECT NO.: BHO 1448 (27)		CHKD: - DFTM: T.D. JOB NO: 23421-014	
P/S VOIDED SLAB DETAILS		DWG. NO: S2	
