

SECTION 641 TRAFFIC SIGNS SUMMARY SHEET

MAINLINE PAVING






RAMP PAVING

IDENTIFICATION	NUMBER OF SIGNS	SIZE		TEXT		FOR SIGN DETAIL SEE STANDARD OR SHEET NUMBER
		WIDTH	HEIGHT			
	2	4	4	LEFT LANE CLOSED 1 MILE		E-8
	6 OR AS REQUIRED	18"	8"	RIGHT		E-8
	2	4	4	LEFT LANE CLOSED 1/2 MILE		E-8
	2	4	5	REDUCED SPEED AHEAD		THIS SHEET
	2 OR AS REQUIRED	4	4	LEFT LANE CLOSED 1500 FEET		E-8
	2	4	4			E-8
	2	4	4			E-8
	AS REQUIRED	4	5	DO NOT PASS		THIS SHEET
	AS REQUIRED	4	5	SPEED LIMIT 40		E-15B
	1	4	5	END SPEED ZONE		THIS SHEET
	AS REQUIRED	4	4	CAUTION PAVEMENT CHANGE	SEE E-6 FOR MATERIALS, ETC.	THIS SHEET
	AS REQUIRED	4	4	BUMP	SEE E-6 FOR MATERIALS, ETC.	THIS SHEET
	2	4	4	ROAD CONSTRUCTION AHEAD		E-2
	2	5	3	ROAD CONSTRUCTION NEXT ----- MILES		E-2
	1	4	4			E-6
	AS REQUIRED	4	4	HIGH OR LOW SHOULDER	" " " " " "	THIS SHEET

IDENTIFICATION	NUMBER OF SIGNS	SIZE		TEXT		FOR SIGN DETAIL SEE STANDARD OR SHEET NUMBER
		WIDTH	HEIGHT			
	AS REQUIRED	4	4	LEFT LANE CLOSED AHEAD		E-8
	AS REQUIRED	18"	8"	RIGHT		E-8
	AS REQUIRED	4	4			E-6

SIGN NOTES: TRAFFIC SIGNS SHOWN ON THIS SHEET ARE TO BE SUBSIDIARY TO ITEM 641, TRAFFIC CONTROL. ADDITIONAL SIGNS, IF REQUIRED THAT ARE NOT DETAILED WILL BE PAID AS ITEM 675.20 OR 675.25 AS DIRECTED BY THE ENGINEER IF ITEMS ARE PART OF THE CONTRACT. PROJECT SIGNS AS PER STANDARD E-2 AND E-6 WILL BE REQUIRED TO ESTABLISH PROJECT LIMITS AND AS RAMP SIGNING. SIGNS SHALL BE ERECTED ON FLANGED CHANNEL STEEL POSTS*

*SIZE = 3 LBS/FT - MAXIMUM

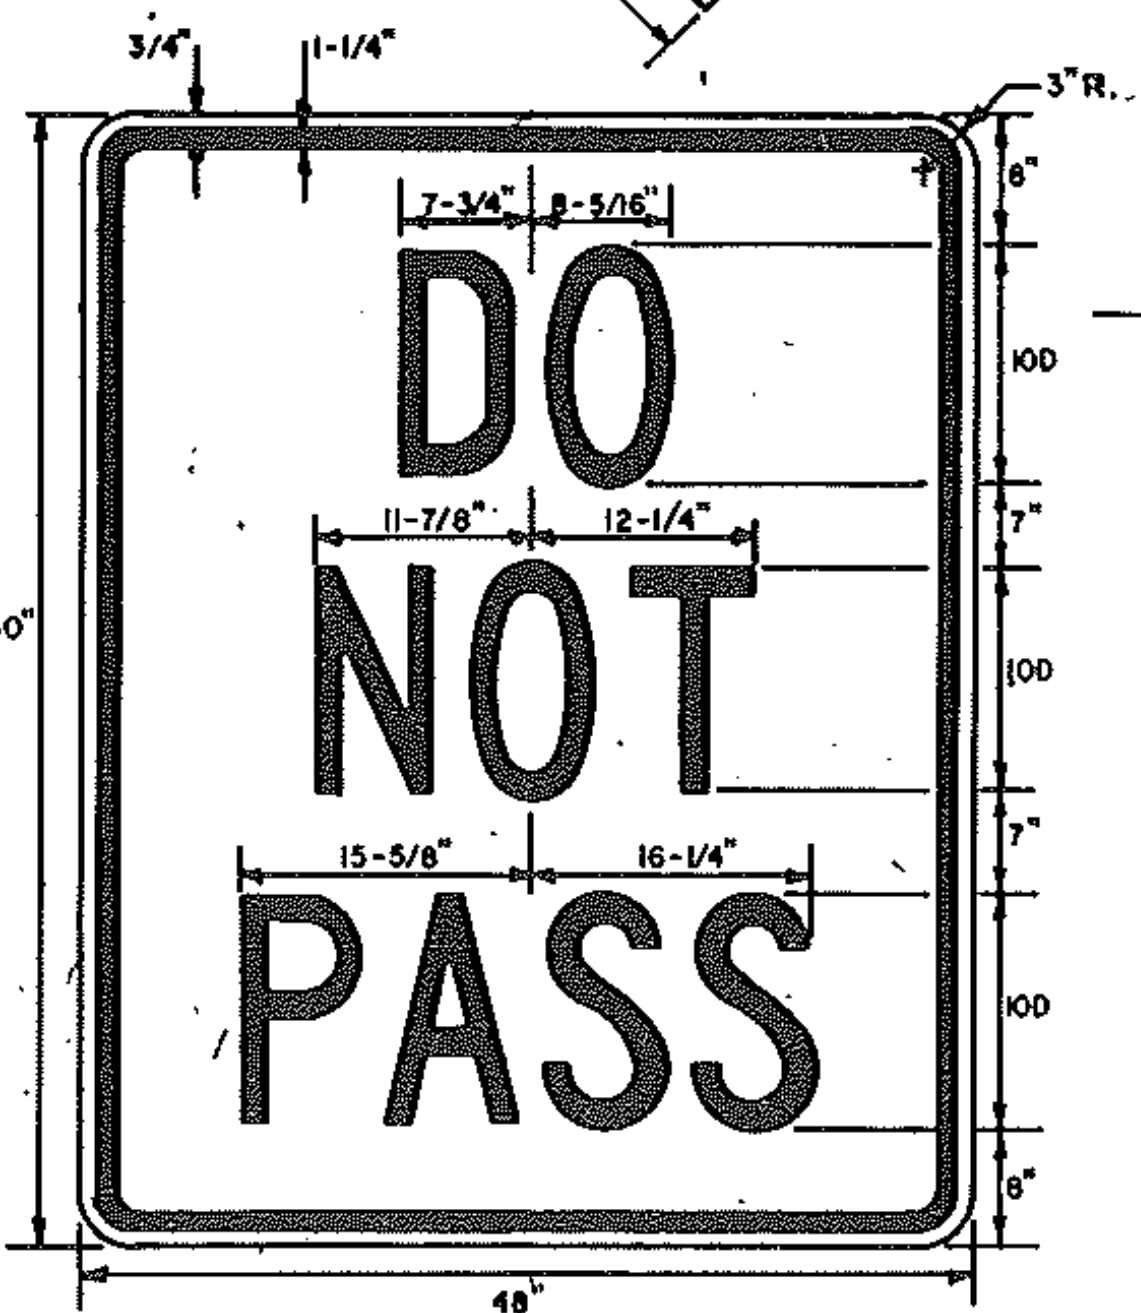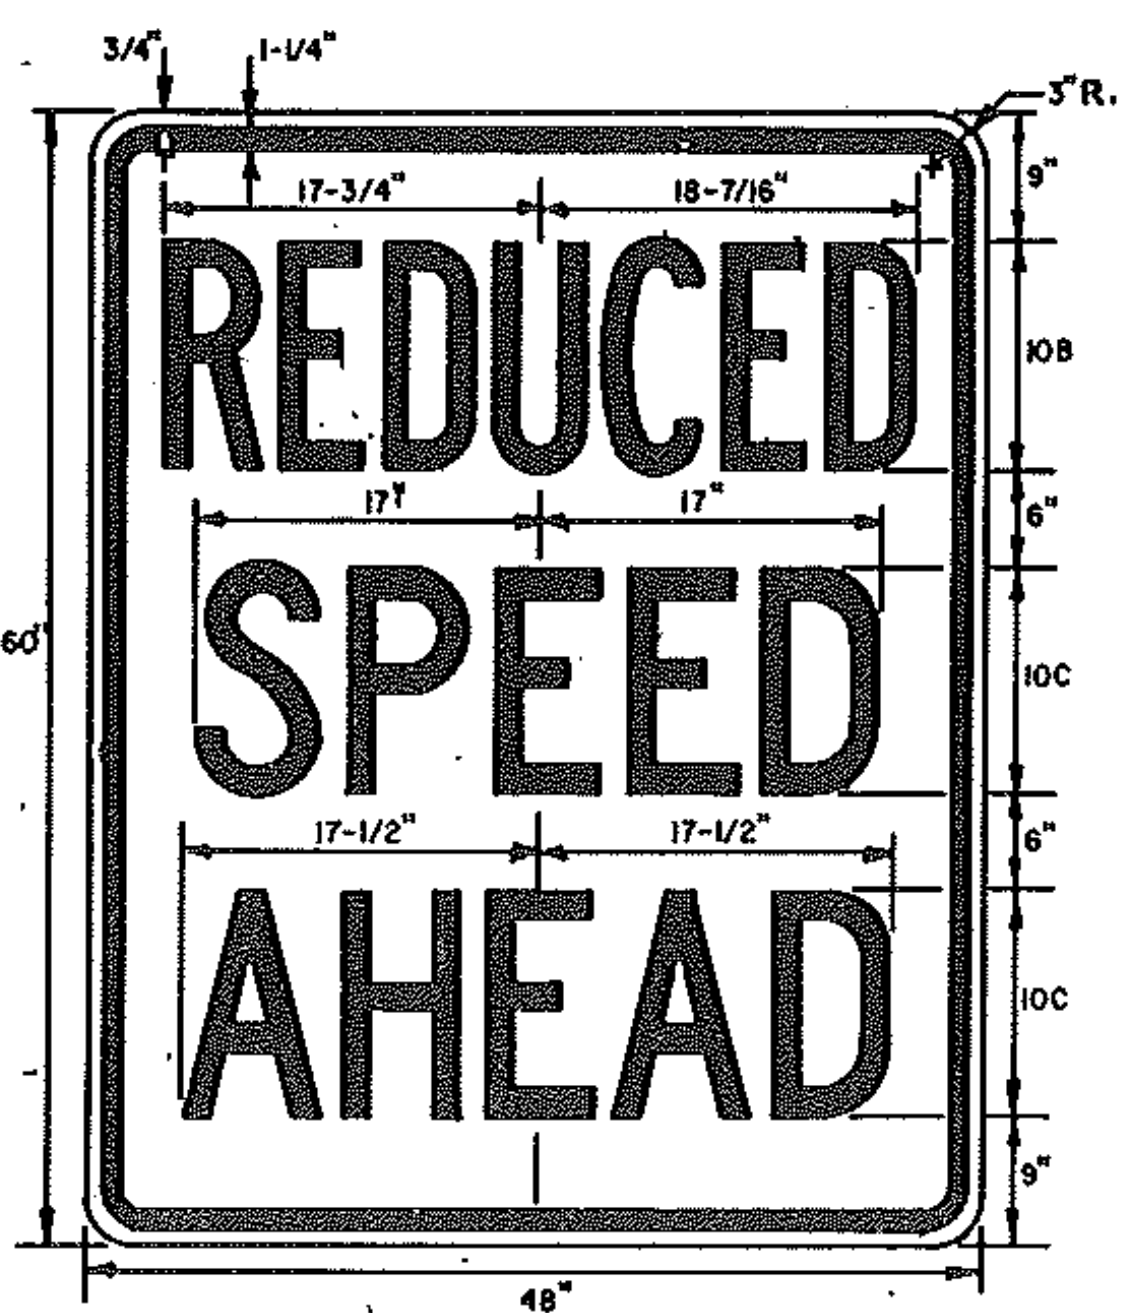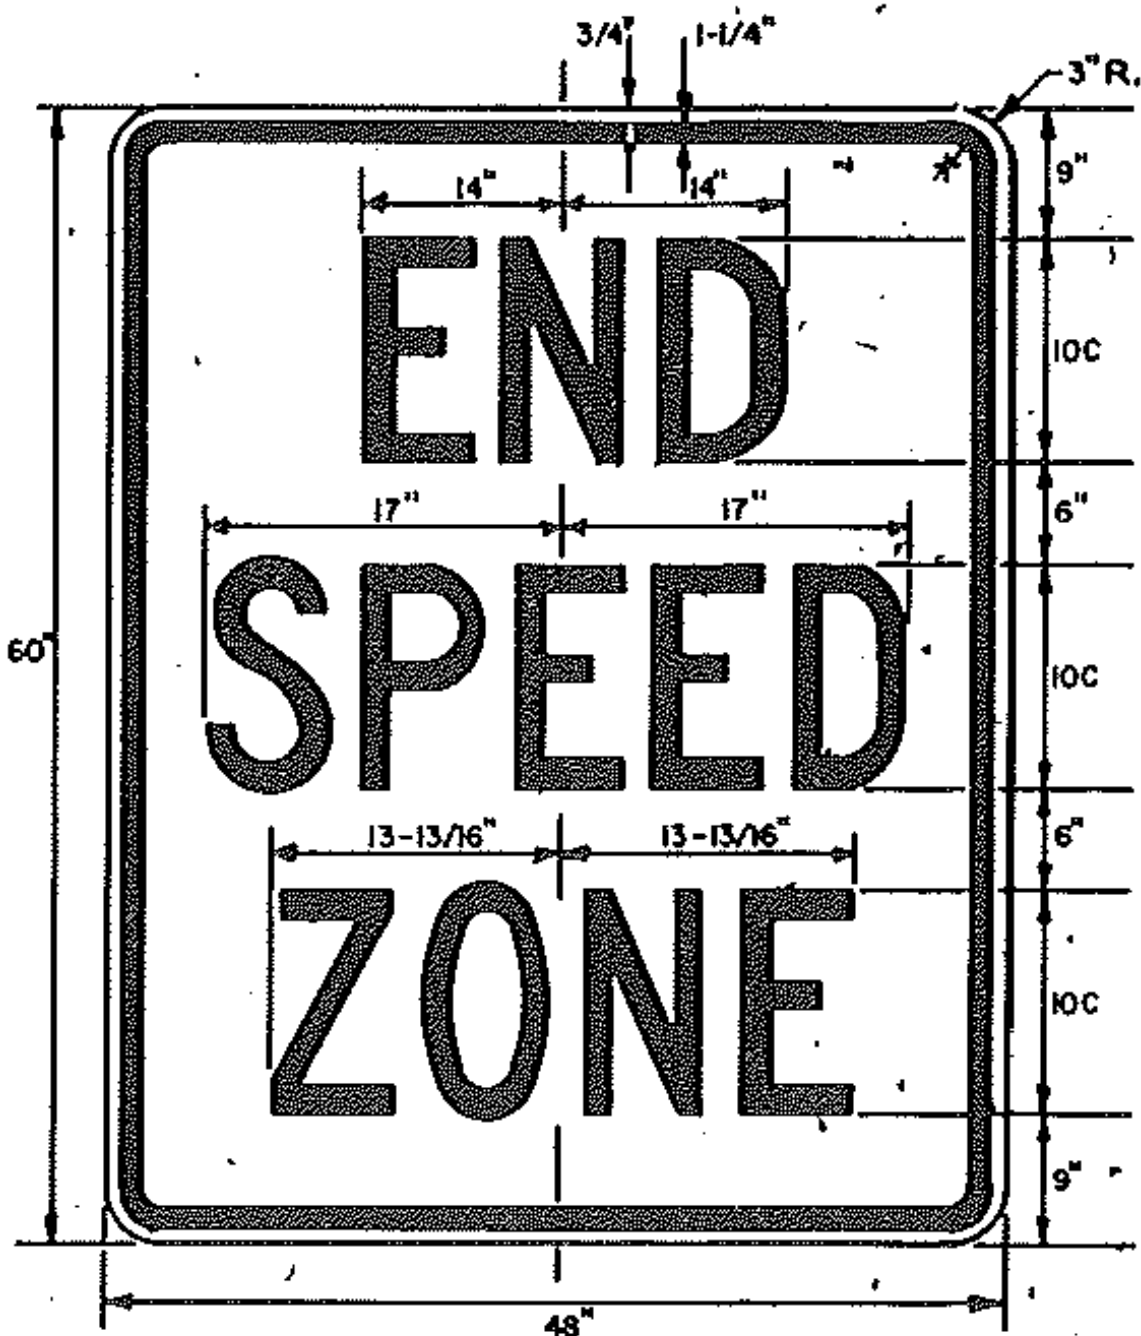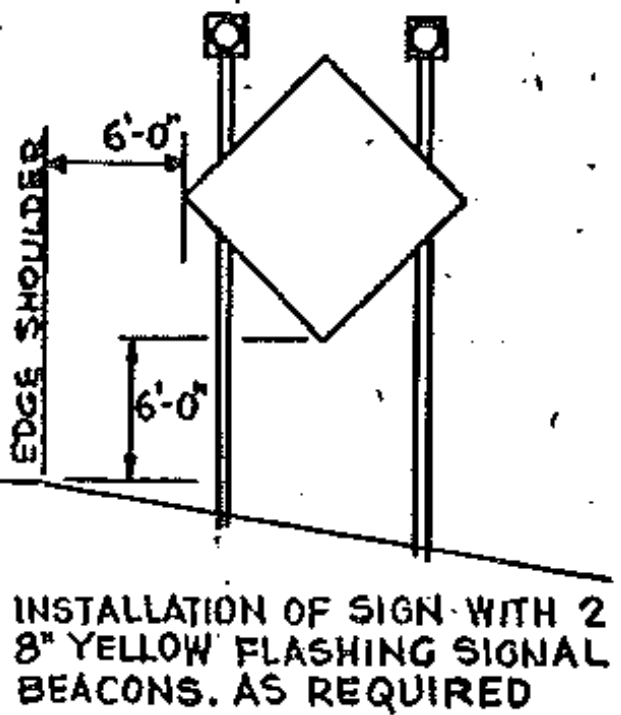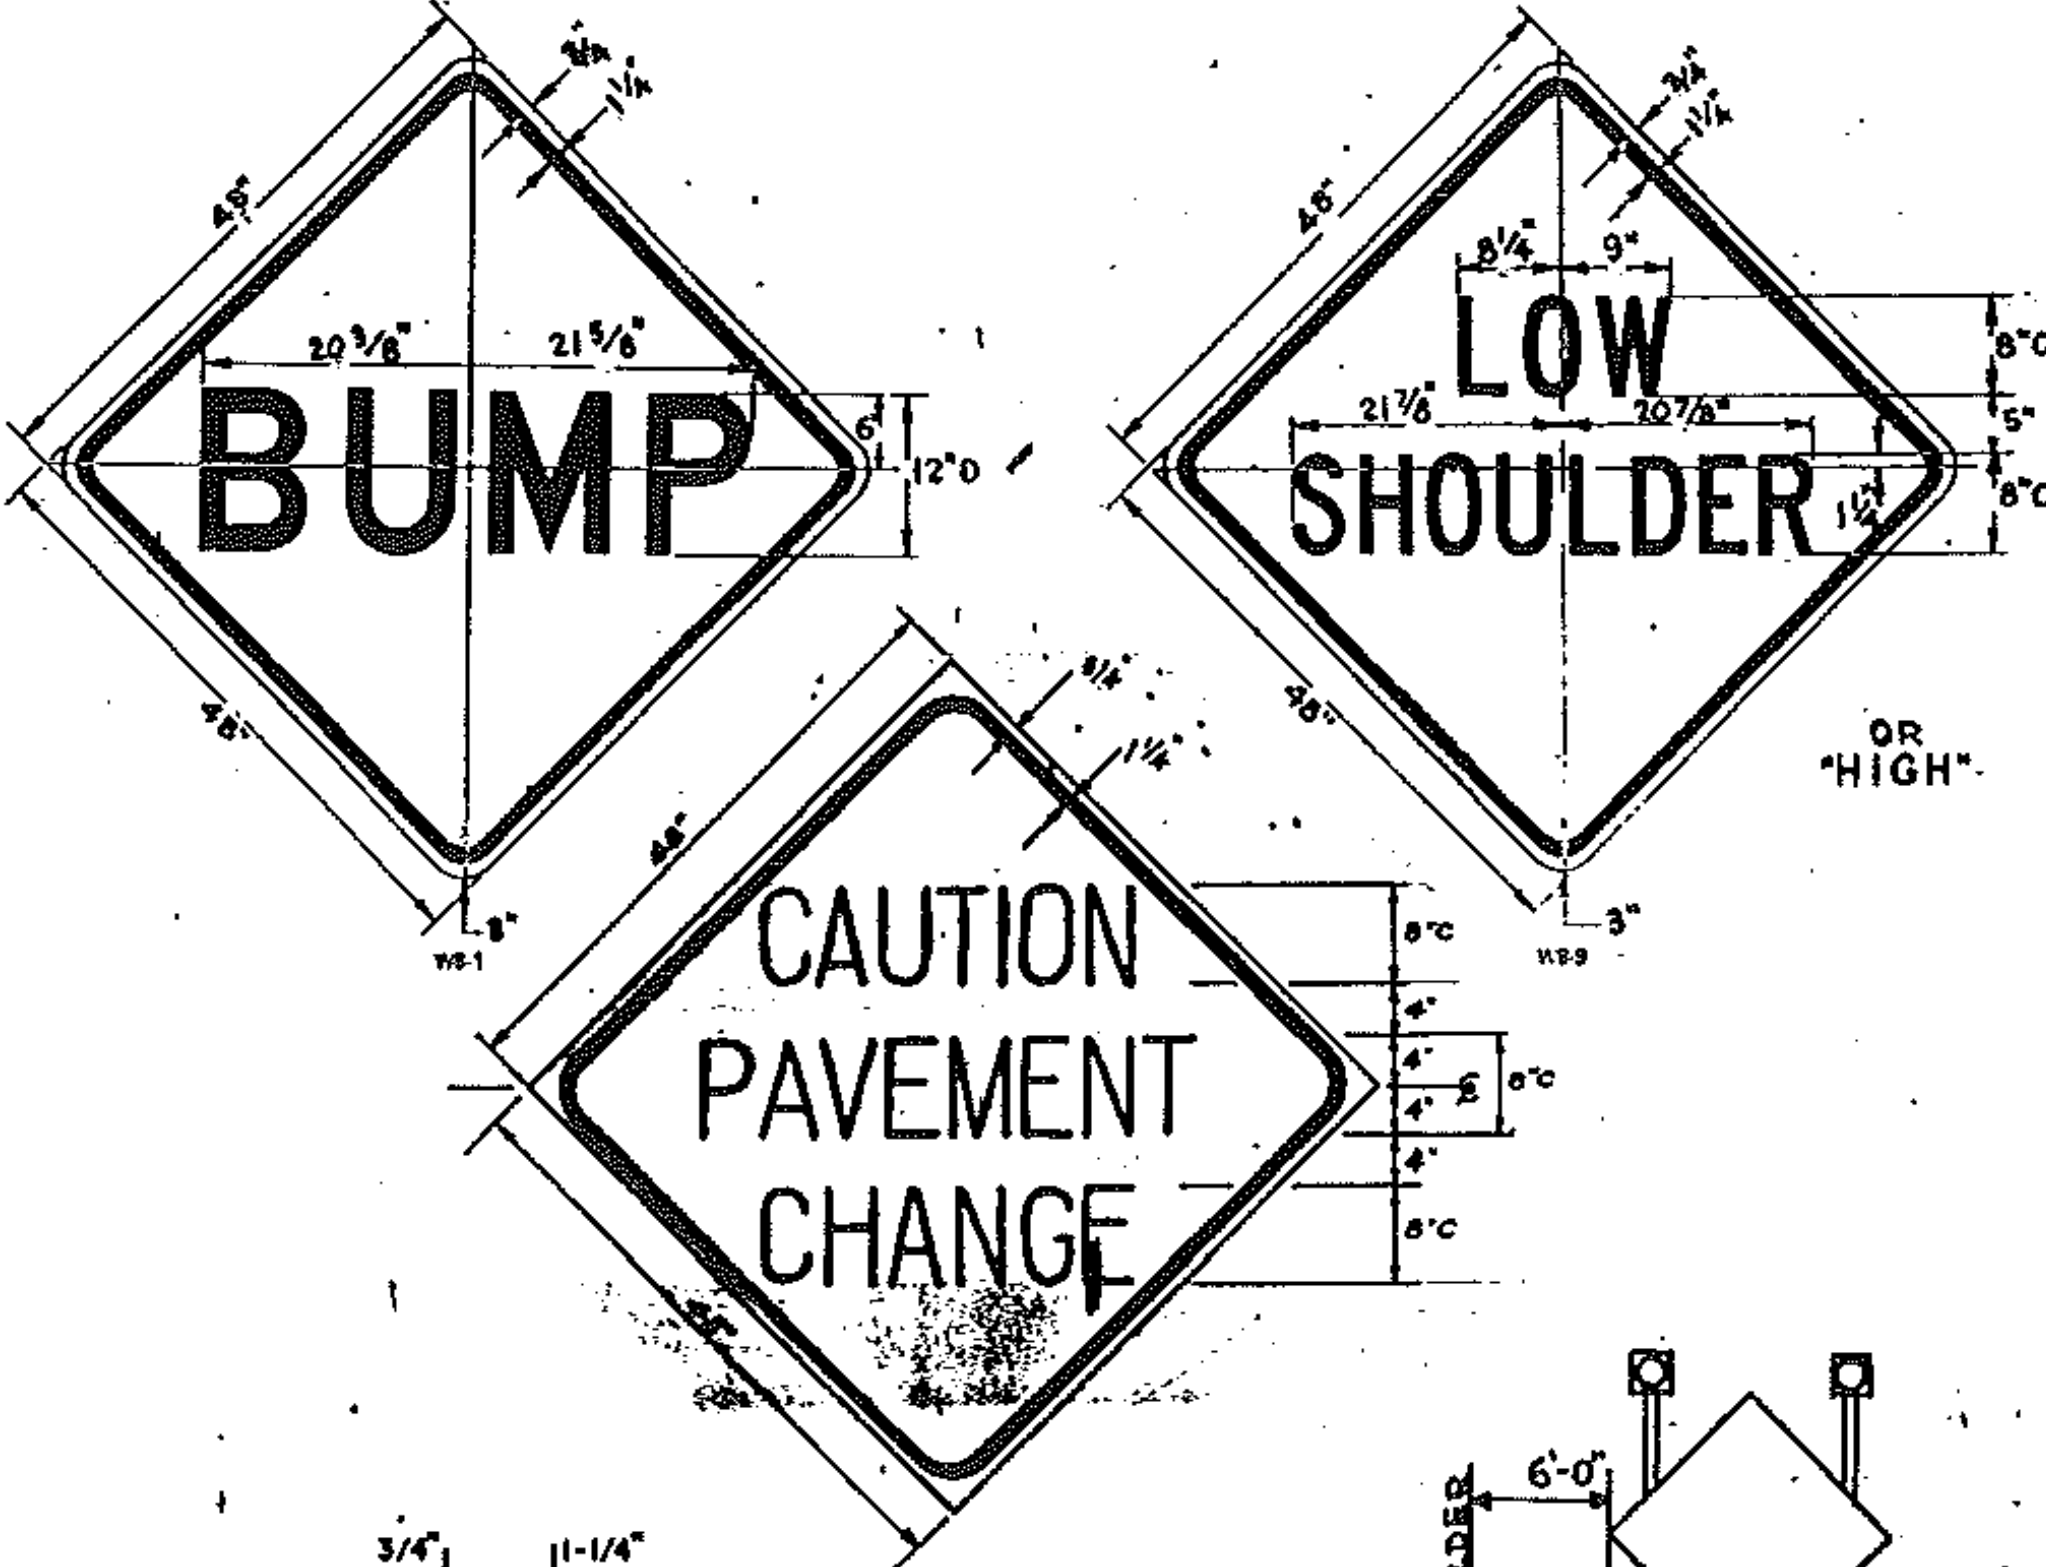

COLORS: LEGEND - BLACK (NON-REFLECTORIZED) BACKGROUND - WHITE (REFLECTORIZED) (SEE STANDARD SHEET E-15B FOR MATERIAL SPECIFICATIONS)

STANDARD E-2 LISTED FOR SIGN DETAIL ONLY, NOT MAINLINE PROJECT SIGNING.

SECTION 641	SURVEYED BY _____ DATE _____
TRAFFIC SIGN	DRAWN BY RPR DATE 2-82
SUMMARY SHEET	TRACED BY LCG DATE 6-82
MAINLINE	MIDDLESEX - WATERBURY
TRAFFIC CONTROL	PROJ. IR NO 089-2(6)
PLAN	SHEET 15 OF 34
