


653.20 - TEMPORARY EROSION MATTING
RAMP A STA 223+50 RT TO RAMP A STA 225+25 RT


653.55 - PROJECT DEMARCATION FENCE
RAMP A STA 223+45 RT TO RAMP A STA 225+30 RT

AREA OF DISTURBANCE
CREST OF LEDGE: 3,506 SF = 0.080 ACRES
DITCH: 1,526 SF = 0.035 ACRES
ACCESS: 1,046 SF = 0.024 ACRES
SHEET TOTAL: 6,078 SF = 0.139 ACRES
PROJECT TOTAL: 86,811 SF = 1.993 ACRES

AREA OF SOLID ROCK EXCAVATION
SHEET TOTAL: 0 SF = 0 ACRES
PROJECT TOTAL: 27,864 SF = 0.639 ACRES

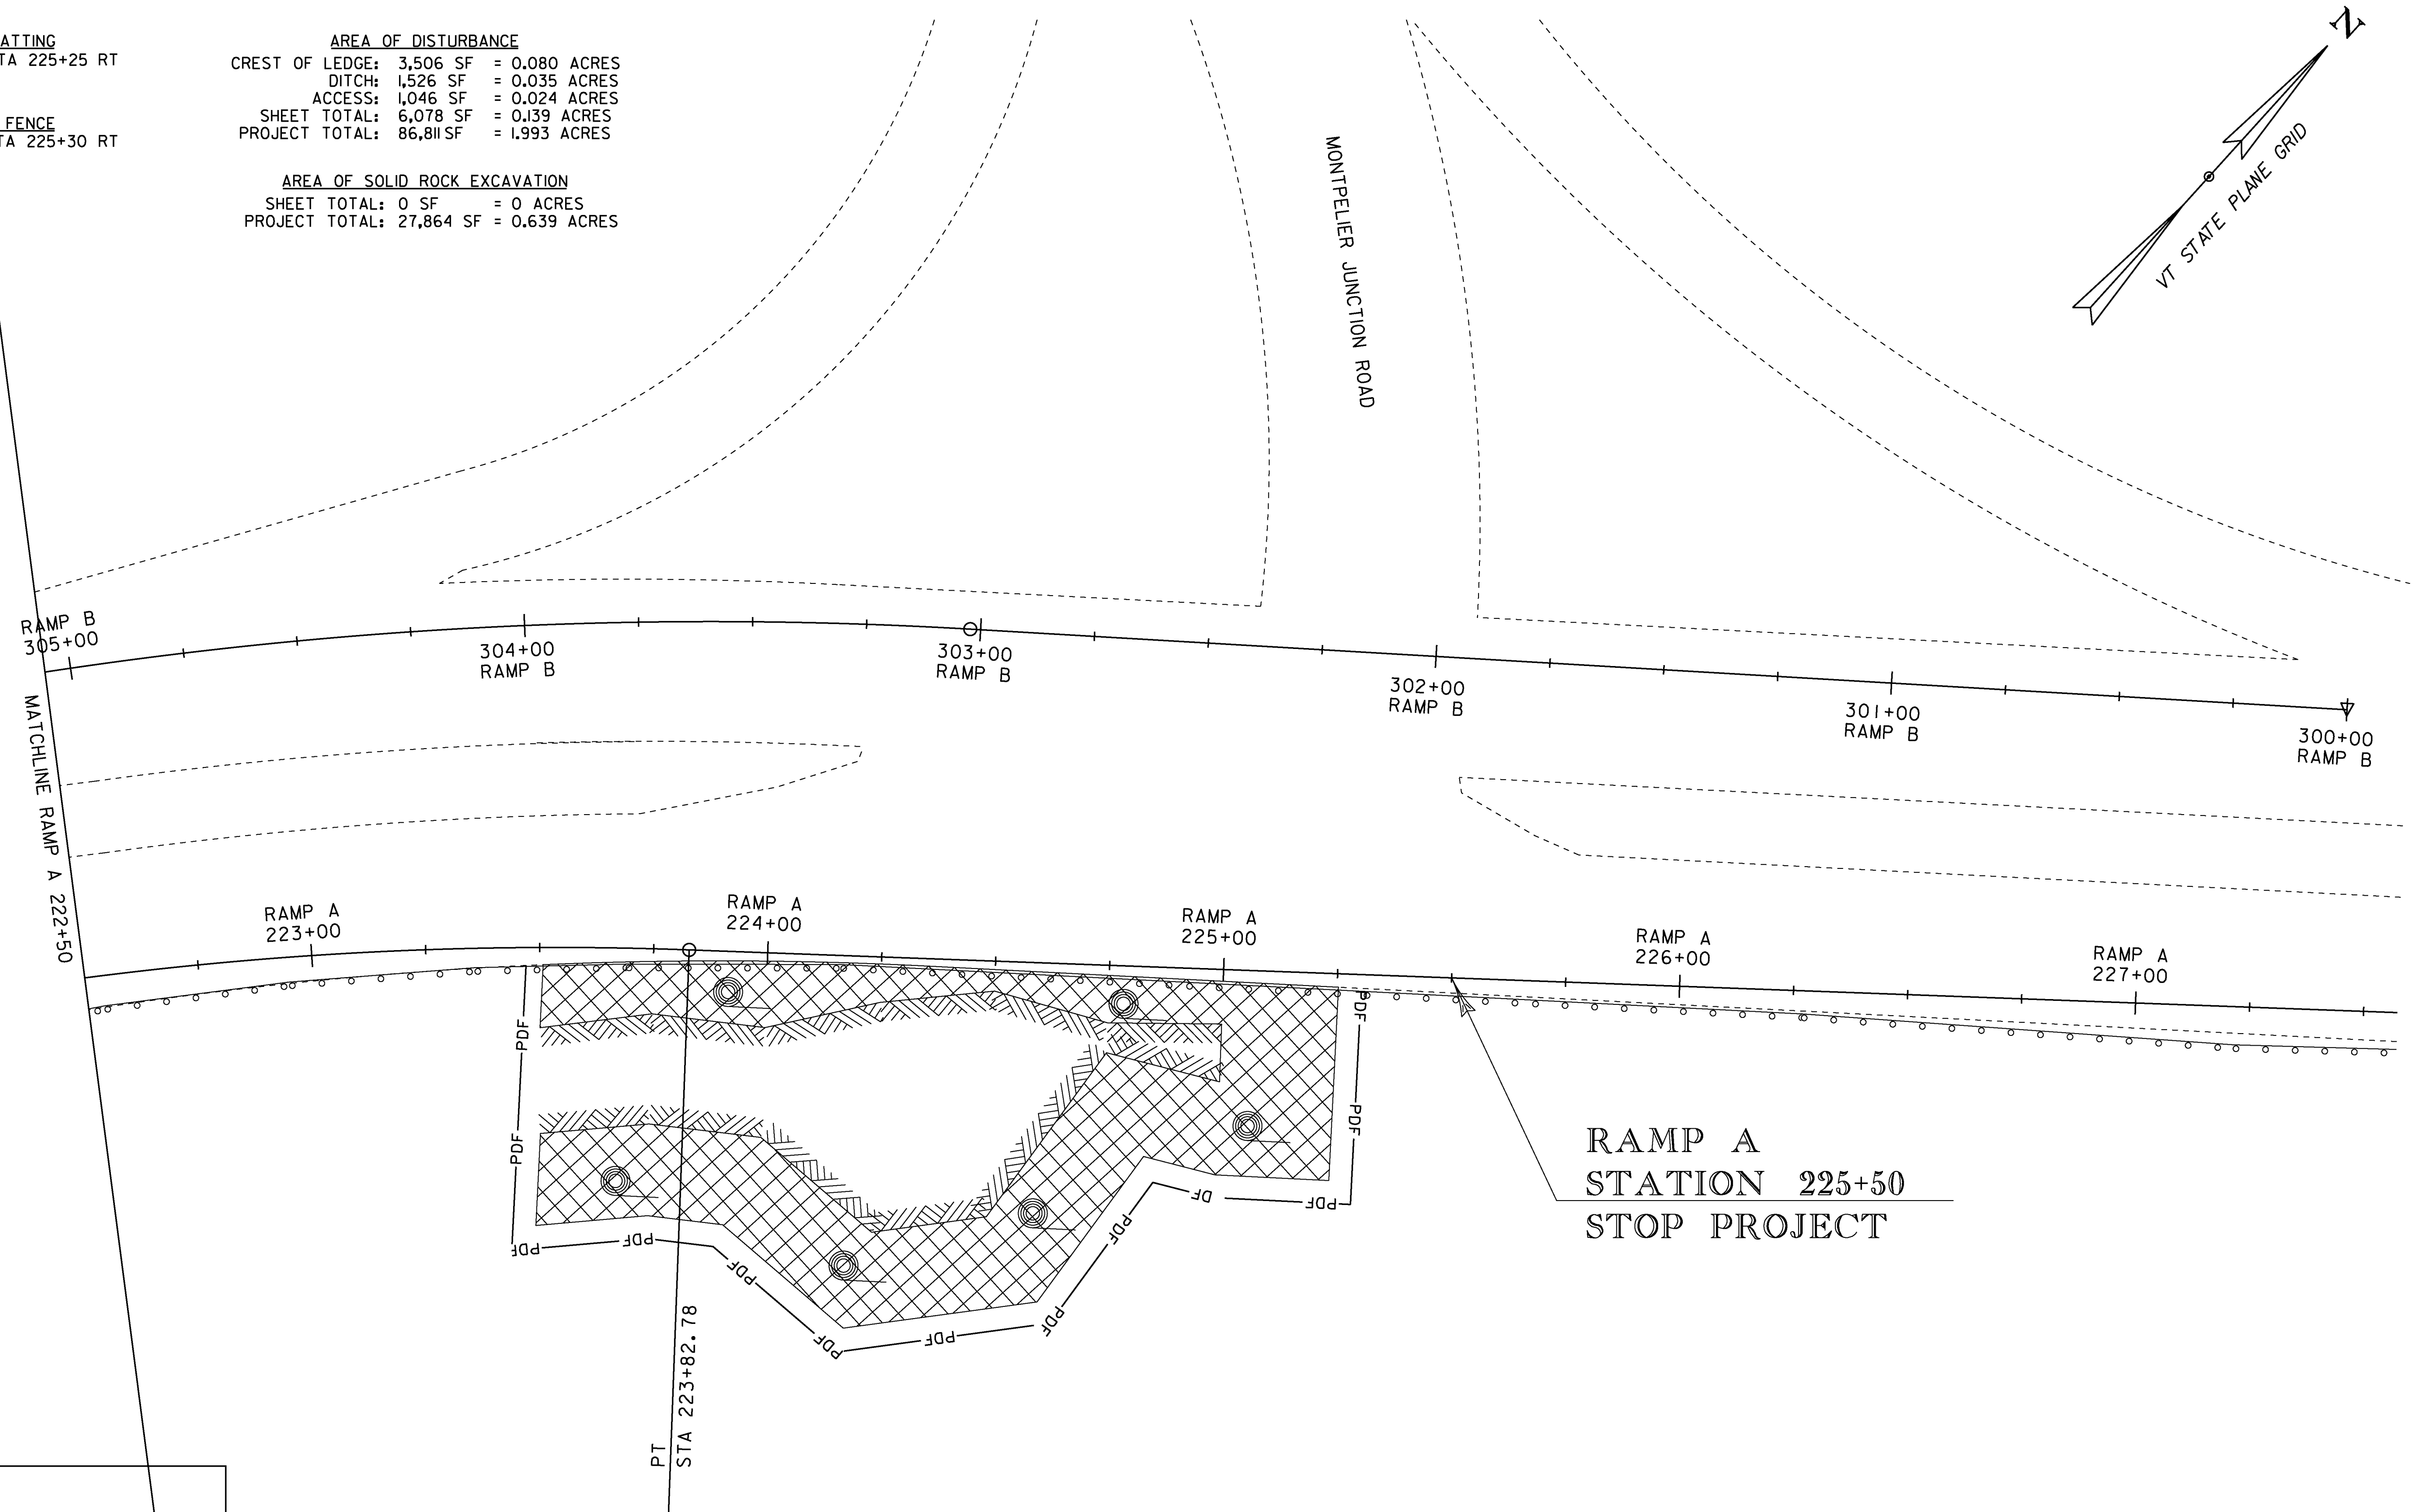

LEGEND

-  SOLID ROCK EXCAVATION
-  EROSION MATTING/LIMITS OF DISTURBANCE
-  PROJECT DEMARCATION FENCE
-  DROP INLET PROTECTION

RAMP A LAYOUT SHEET 4

0 20 40
SCALE IN FEET

PROJECT NAME: MONTPELIER
PROJECT NUMBER: NH 028-2(9)

FILE NAME: \\b066\Design\d\\b066bdr\env.dgn PLOT DATE: 24-MAY-2013
PROJECT LEADER: P. PELOQUIN DRAWN BY: P. PELOQUIN
DESIGNED BY: P. PELOQUIN CHECKED BY: A. BOMBARDIER
EPSC LAYOUT SHEET 5 SHEET 48 OF 62
